



Grove St Update for the Board of Education

June 21, 2018






Before....





Demo before start new



District Self Performed Work in Progress

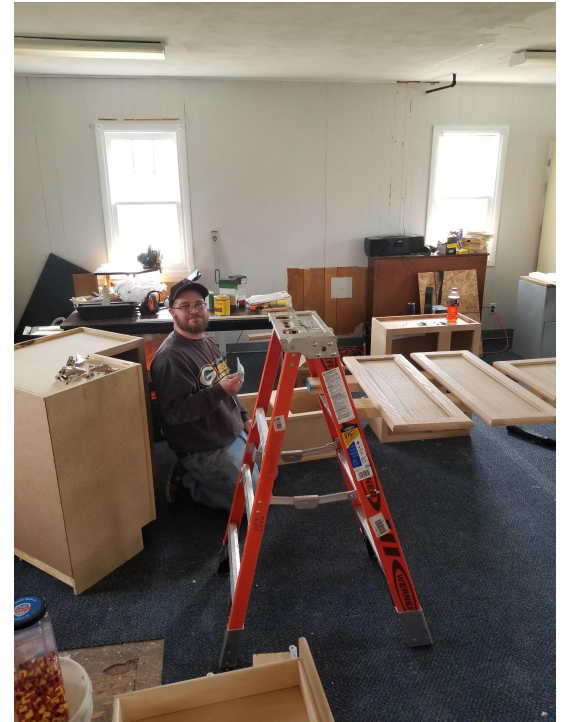

District Self Performed Work in Progress

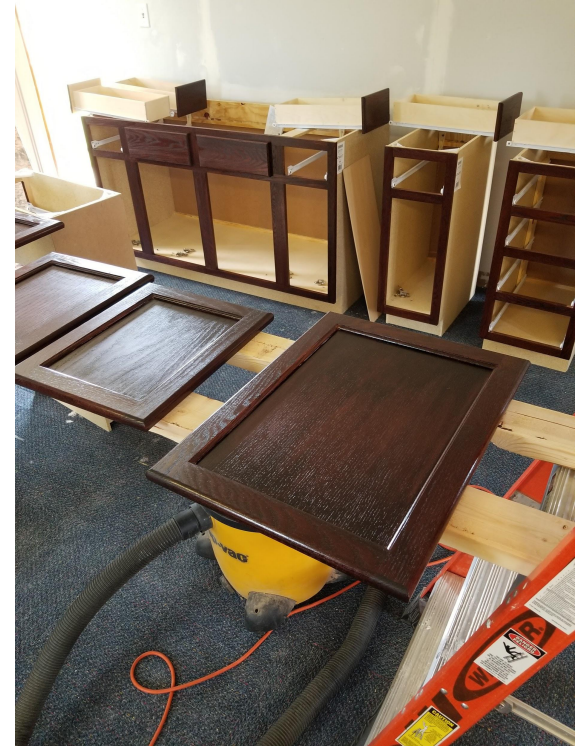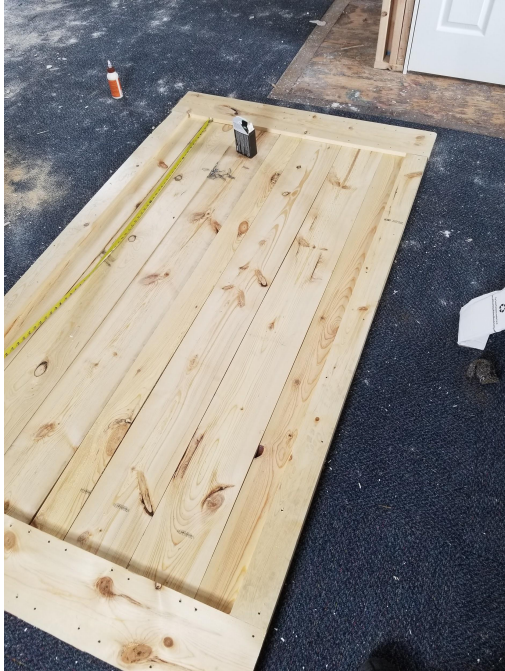



Work in Progress




Finished Product



Finished Product



Finished Product

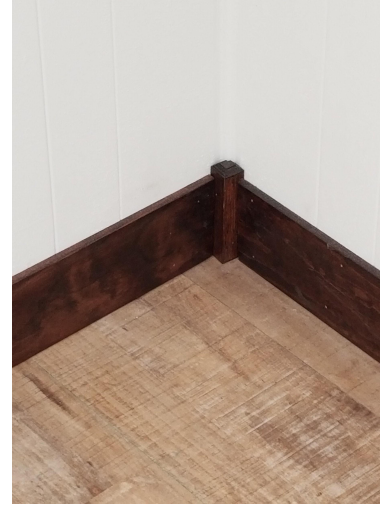



Finished Product





Finishing Touches



Concrete exterior walk (rain has cancelled this all week, scheduled for Friday 6/22/18)*

Security Cameras (installing Friday 6/22/18)

Install ADA Vertical Grab Bar in Restroom (installing Friday 6/22/18)*

Repair Exterior Foundation Cracks (Scheduled week of 6/25/18)

Paint Exterior

Move in Crossroads Items (Friday 6/22/18)

Purchase / Install Appliances (Week of 6/25/18)

Purchase / Install “Crossroads/Pathways” Sign to match other District Sites

Receive Occupancy From City Building Inspector - Goal of 6/22/18

Grand Opening! - Start of 2018-19 School Year



Who Did What?

Demo - District Staff

Cabinets / Countertops - District Staff

Plumbing - District Staff

Sliding Barn Door - District Staff

Flooring Install - District Staff

Technology Install- District IT Staff

Concrete - Allard Asphalt

Security Cameras - ESI

Masonry - Holton Brothers

HVAC - Trane / Illingworth-Kilgust

Doors / Windows - Fort Glass

Security / Fire Alarms - PerMar

Electrical - Ready Electric
